PROJECT PLANNING PHASE

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	25 October 2026
Team ID	Individual project
Project Name	HotelPro (Hotel Management System)
Maximum Marks	5 Marks

Product backlog, sprint schedule and estimation (4 marks)

The work is split into four sprints of 20 story points each (80 points in total). Each sprint delivers a working part of HotelPro. Team members: one (individual project).

Product backlog and sprint schedule

Sprint	Functional requirement (epic)	User story no.	User story / task	Story points	Priority	Team members
Sprint-1	Authentication and room inventory	USN-1	As a user, I can register an account.	3	High	Self
		USN-2	As a user, I can log in securely with a token-based session.	3	High	Self
		USN-3	As the system, I enforce guest, staff and admin roles on protected routes.	3	High	Self
		USN-4	As an admin, I can add, edit, delete and close rooms.	5	High	Self
		USN-5	As a guest, I can browse the list of rooms.	3	High	Self
		USN-6	As a guest, I can view the details of a room.	3	Medium	Self
Sprint-2	Search and booking	USN-7	As a guest, I can search rooms by dates, guests and type.	5	High	Self
		USN-8	As a guest, I can book a room and see the total price.	5	High	Self
		USN-9	As the system, I prevent double bookings for the same dates.	5	High	Self
		USN-10	As a guest, I can view my bookings.	3	High	Self
		USN-11	As a guest, I can cancel an upcoming booking.	2	Medium	Self
Sprint-3	Payments and front-desk operations	USN-12	As a guest, I can pay online (simulated gateway).	5	High	Self
		USN-13	As staff, I can check a guest in.	3	High	Self
		USN-14	As staff, I can check a guest out.	2	High	Self
		USN-15	As staff, I can record a pay-at-hotel payment.	3	Medium	Self
		USN-16	As the system, I mark a cancelled paid booking as refunded.	2	Medium	Self
		USN-17	As staff, I can view and filter all bookings.	5	High	Self
Sprint-4	Dashboard, security and deployment	USN-18	As an admin, I can see occupancy, arrivals and revenue.	5	High	Self
		USN-19	As an admin, I can see the list of guests.	3	Medium	Self
		USN-20	As the system, I apply security headers, rate limiting and input validation.	5	High	Self

Sprint	Functional requirement (epic)	User story no.	User story / task	Story points	Priority	Team members
		USN-21	As a user, I get a responsive interface with clear error messages.	3	Medium	Self
		USN-22	As the owner, I deploy the app and document setup in a README.	4	High	Self

Project tracker, velocity and burndown chart

Planned schedule. Each sprint is 6 days long with 20 story points.

Sprint	Total story points	Duration	Sprint start date	Sprint end date (planned)	Story points completed (as on planned end date)	Sprint release date (actual)
Sprint-1	20	6 days	28 September 2026	03 October 2026		
Sprint-2	20	6 days	05 October 2026	10 October 2026		
Sprint-3	20	6 days	12 October 2026	17 October 2026		
Sprint-4	20	6 days	19 October 2026	24 October 2026		

Velocity. Average velocity = total story points / number of sprints = 80 / 4 = **20 story points per sprint**, or about 3.3 points per day over a 6-day sprint.

Planned burndown chart

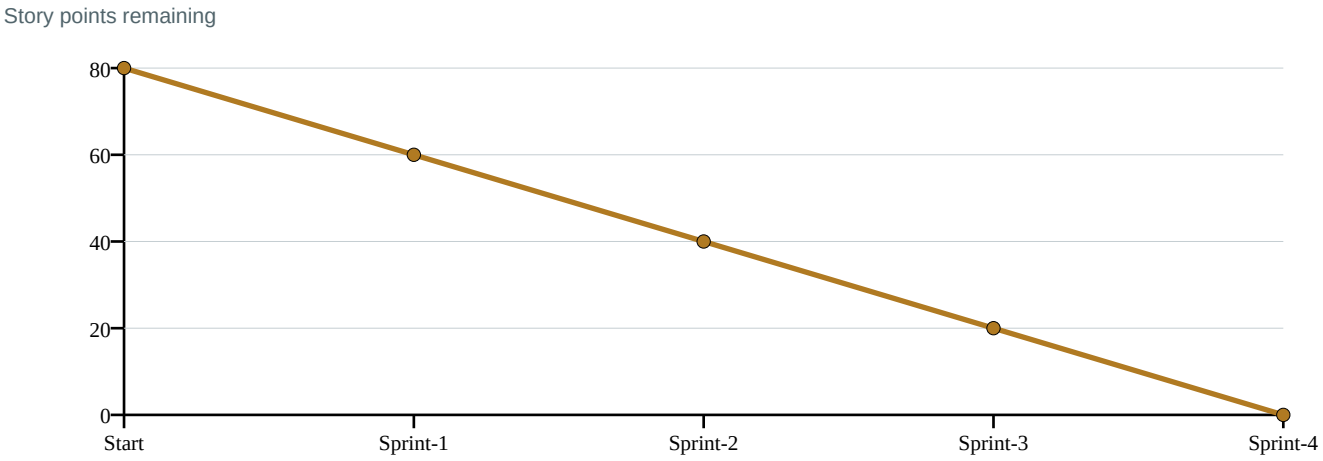

Figure 1. Planned burndown: 80 story points reduced by 20 at the end of each sprint.

Point in time	Start	End of Sprint-1	End of Sprint-2	End of Sprint-3	End of Sprint-4
Story points remaining (planned)	80	60	40	20	0

Reference: atlassian.com/agile/tutorials/burndown-charts
